

PVUNL Unit -3 Updates as on 23-09-26



Major Critical Issues – Unit 3



Present BHEL Commitment – Unit 3 commissioning by May-27. PVUNL requested timelines – Unit 3 – Boiler Light up – 05.12.26, Sync – 31.01.27 and Full load – 25.02.27, Trial operation – 15.03.27

With material supplies liquidation progressively by November, Unit 3 trial operation can be done by 15.03.27

Alternate agency award and mobilization in Piping expected by Sep end. Decision to be made regarding ESP, Ducting and Insulation works

Manpower - Texcel

Boiler, ESP and PCP

Required: 1,650

Available: 1,050

Deficit: 500

Material Supply

Liquidation by Nov

Duct: 700 MT Pending (approx.
400MT supplied in last 2 months)

Roof Enclosure: 130 MT
(1st lot dispatch commitment by 30.09.26)

Structure – 1800MT
(Supplies from Kharkiyon yet to start)

Ash Handling

6 months for 1 Unit

4 months erection (Sep-Dec)

2 months commissioning - (Jan-Feb)

Extended hour works/Multiple work shifts for existing manpower in ACC, PCP, Boiler, ESP and Civil works



PVUNL – Ph -1 (3*800MW) - EPC Award – 08.03.2018

- Trial run Schedule – Unit 1 and Unit 2 - Completed; Unit 3 – Mar'27

Physical Progress

U#1 – 99% (COD – 05.11.25)
 U#2 – 98% (COD – 26.06.26)
 U#3 – 71%
 BOP Including FGD – 76%

Time Overrun – (L2/Act/Ant)

U#1 – 43 months (Mar '22/ Oct '25)
 U#2 – 42 months (Sep '22/ May '26)
 U#3 – 47 months (Mar'23/ Mar '27)

Financial Progress

Original Cost – 18668cr /RCE-1 – 20301.57cr/ RCE-2-21872cr
 Accrual Capex - 19405 cr
 Cash capex – 16441 cr

- **Unit 3 – Boiler Light up – Dec'26, Sync – Jan'27 and Full load - Mar'27, Trial operation – Mar'27**
- Ash mound – Ash dumping through temporary road in progress. Through permanent road (Nalkari Bridge) targeted by Nov'26.
- Ash mound & Corridor works in progress, Target commissioning by Feb-27
- **Ash Mound issues** – Stage 2 Forest clearance for Ash Mound (19 Ha) still pending. EDS compliance submitted, CA land mutation clearance (GOJH Cabinet approval): Proposal cleared by Commissioner Hazaribaug and submitted to Secy Revenue, GoJH.
- **Ash Corridor** (Ash evacuation from Plant to Ash Mound)-2.42 Ha – Forest Stg 1 clearance granted. Working permission granted on 25.04.26 and work in progress.



Project Timeline



EPC Award: 08.03.2018

Major Milestones	Boiler Drainable HT	TG Box up	TG oil flushing completion	TG on Barring	Boiler NDHT	Boiler Chemical cleaning completion	Boiler Light-up	Steam Blowing Completion	Sync.	Full Load.	Commissioning/ TO
U#1 (L2/ Ant./ Act.)	Jan'21/ Mar'23	May'21/ Mar'23	Jul'21/ Jan'24	Aug'21/ May'24	Jun'21/ Apr'24	Jul'21/ Aug'24	Jul'21/ Aug'24	Sep'21/ Dec'24	Nov'21/ 11.03.25	Dec'21/ 13.08.25	Mar'22/ 16.10.25
U#2	Jul'21/ Sep'23	May'21/ Mar'24	Jan'22/ Jul'25	Feb'22/ Aug'25	Dec'21/ 05.06.25	Jan'22/ 18.09.25	Jan'22/ Nov'25	Mar'22/ Dec'25	May'22/ 17.03.26	Jun'22 27.03.26	Sep'22/ 11.05.26
U#3	Jan'22/ Aug'26 17.08.26	May'22/ Nov'26 30.11.26	Jul'22/ Nov'26 18.11.26	Aug'22/ Nov'26 25.11.26	Jun'22/ Nov'26 18.11.26	Jul'22/ Nov'26 20.11.26	Jun'22/ Dec'26 05.12.26	Sep'22/ Dec'26 31.12.26	Nov'22/ Jan'27 31.01.27	Dec'22/ Mar'27 10.03.27	Mar'23/ Mar'27 15.03.27



27-03-26 Unit 2 achieved full load



Unit 2 full load 800 MW achieved on 27.03.2026
Congratulations Team PVUNL



एनटीपीसी
NTPC

A Maharatna Company

Project Review and Internal Monitoring System
PRIMS

Project
Monitoring
Centre

23/05/2026 10:36:27

From Boiler Light Up to Full Load duration

Sno	Project	Boiler Light Up	Full Load	Duration(In Days)	Duration(In Months)
800					
1	Patratu STPP U# 2	25-Nov-25	27-Mar-26	122	4
2	Kudgi-I U# 2	30-Oct-16	23-Mar-17	144	5
3	Kudgi-I U# 3	9-Apr-17	12-Mar-18	337	11
4	Darlipali-I U# 1	28-Oct-18	2-Oct-19	339	12
5	Patratu STPP U# 1	31-Aug-24	13-Aug-25	347	12
6	Kudgi-I U# 1	20-Dec-15	25-Dec-16	371	12
7	Telangana Ph1 U# 1	30-Jun-22	23-Jul-23	388	13
8	Telangana Ph1 U# 2	1-Dec-22	3-Feb-24	429	14
9	Lara-I U# 1	1-Jan-17	23-Mar-18	446	14
10	Gadarwara-I U# 1	27-Apr-17	13-Oct-18	534	18
11	Lara-I U# 2	24-Dec-18	4-Jul-20	558	19
12	Darlipali-I U# 2	24-Oct-19	24-May-21	578	19
13	Gadarwara-I U# 2	31-Dec-18	19-Jan-21	750	25

Benchmark across all 800MW units – 122 days BLU to FL



11-05-26 Unit#2 Trial Operation completion



Project Review and Internal Monitoring System
PRIMS

Project
Monitoring
Centre

23/05/2026 10:40

From Boiler Light Up to TOC duration

Sno	Project	Boiler Light Up	TOC	Duration(In Days)	Duration(In Mnths)
800					
1	Patratu STPP U# 2	25-Nov-25	11-May-26	167	6
2	Kudgi-I U# 3	9-Apr-17	3-May-18	389	13
3	Patratu STPP U# 1	31-Aug-24	16-Oct-25	411	14
4	Darlipali-I U# 1	28-Oct-18	30-Dec-19	428	14
5	Telangana Ph1 U# 1	30-Jun-22	5-Sep-23	432	15
6	Telangana Ph1 U# 2	1-Dec-22	11-Feb-24	437	14
7	Lara-I U# 2	24-Dec-18	12-Jul-20	566	19
8	Darlipali-I U# 2	24-Oct-19	21-Jul-21	636	21
9	Gadarvara-I U# 1	27-Apr-17	29-Mar-19	701	23
10	Gadarvara-I U# 2	31-Dec-18	16-Feb-21	778	26
11	Lara-I U# 1	1-Jan-17	2-Mar-19	790	26

Benchmark across all 800MW units – 167 days BLU to ToC



THANK YOU

पीवीयुएन
PVUN



पीवीयुएन
PVUN

Manpower Status - Unit 3



Agency	Required	Available on 09-07-26	Available on 21-07-26	Available on 08-08-26	Available on 23-09-26	Shortfall	Major Works Affected
Texcel- Boiler	1250	800	850	850	800	450	Non-drainable joints, Ducting, Roof enclosure, Platform works, Intermediate str
Texcel- Piping	400	120	200	200	250	150	MS/CRH/HRH joints. June:9 joints.July-28 Balance ~320 critical joints
A K Singhania	350	270	240	240	320	30	MPH RCC Columns, SG/MPH area paving
ElectroMech	150	130	100	0 60 (Rudra)	30 60 (Rudra)	60	ESP-CR, Drains and Paving works, BA Int silo, ISH, AHP MCC 3
Navnirman	400	320	320	240	280	120	ACC Night works yet to start
Sriram	300	40	75	80 (Elec) 30 (C&I)	130 (Elec) 70 (C&I)	100	*Electrical Labor license – 200 manpower *C&I Labor license – 70
Alpha	150	50	50	60	70	80	*2 shift working in TG TG Piping works to be started
Total	3000	1730	1835	1760	2010	990	



ACC work progress



- Erection completion of ACC Street 4,5,6,7 – Fan 1-4 in September
- GT erection planned from mid Oct end

ACC – 4000/10800 MT (36%)

Manpower deployed – 300.
Required – 400.
Common Duct ATT – 26.12.26

Description	Erection	ATT
Street-1	Completed -8/9	30.09.26
Street-2	Completed -8/9	20.09.26
Street-3	Completed -8/9	10.10.26
Street-4	Oct – UD (4 nos)	05.11.26
Street-5	Oct – UD (4 nos)	15.11.26
Street-6	Oct end - UD (2 nos)	15.12.26
Street-7	Nov end - UD (2 nos)	31.12.26
Street-8	Dec end –Not started	14.01.27



Power Cycle Piping work progress





S. No.	System	Total Joints	Completed	Balance Joints	Present Gangs
1	MS System	146	56	90	5
2	MS to PRDS	26	9	17	1
3	HRH System	95	10	85	0
Total		267	75	192	6
4	HPBP System u/s	23	8	15	1
5	LBBP System	49	6	43	1
		72	14	58	2
6	CRH System	87	14	73	0
7	BFD System	661	158	503	4
Total		748	172	573	4
8	IA/ SA	---	219		3
9	TG-DMCW	---	238		3
10	SG-DMCW	---	38		3
11	CD Bay Structure		---		2
Total					23

No	Description	Unit	Total Joints	Completed	Balance
1	Erection Tonnage	MT	4172	1198.2	2973.8
2	P-91 /P-92 Joints	Nos.	339	89	250
3	HP Piping Joints	Nos.	2199	172	2027
4	LP Piping Joints	Nos.	2892	495	2397

Gangs Detail			
No.	Description	Total	Present
1	Fitter Gangs	25	23
2	Foreman Gangs	4	4
3	Scaffolder Gangs	3	3
4	IBR welder Gangs	10	10
5	LP welder Gangs	5	5



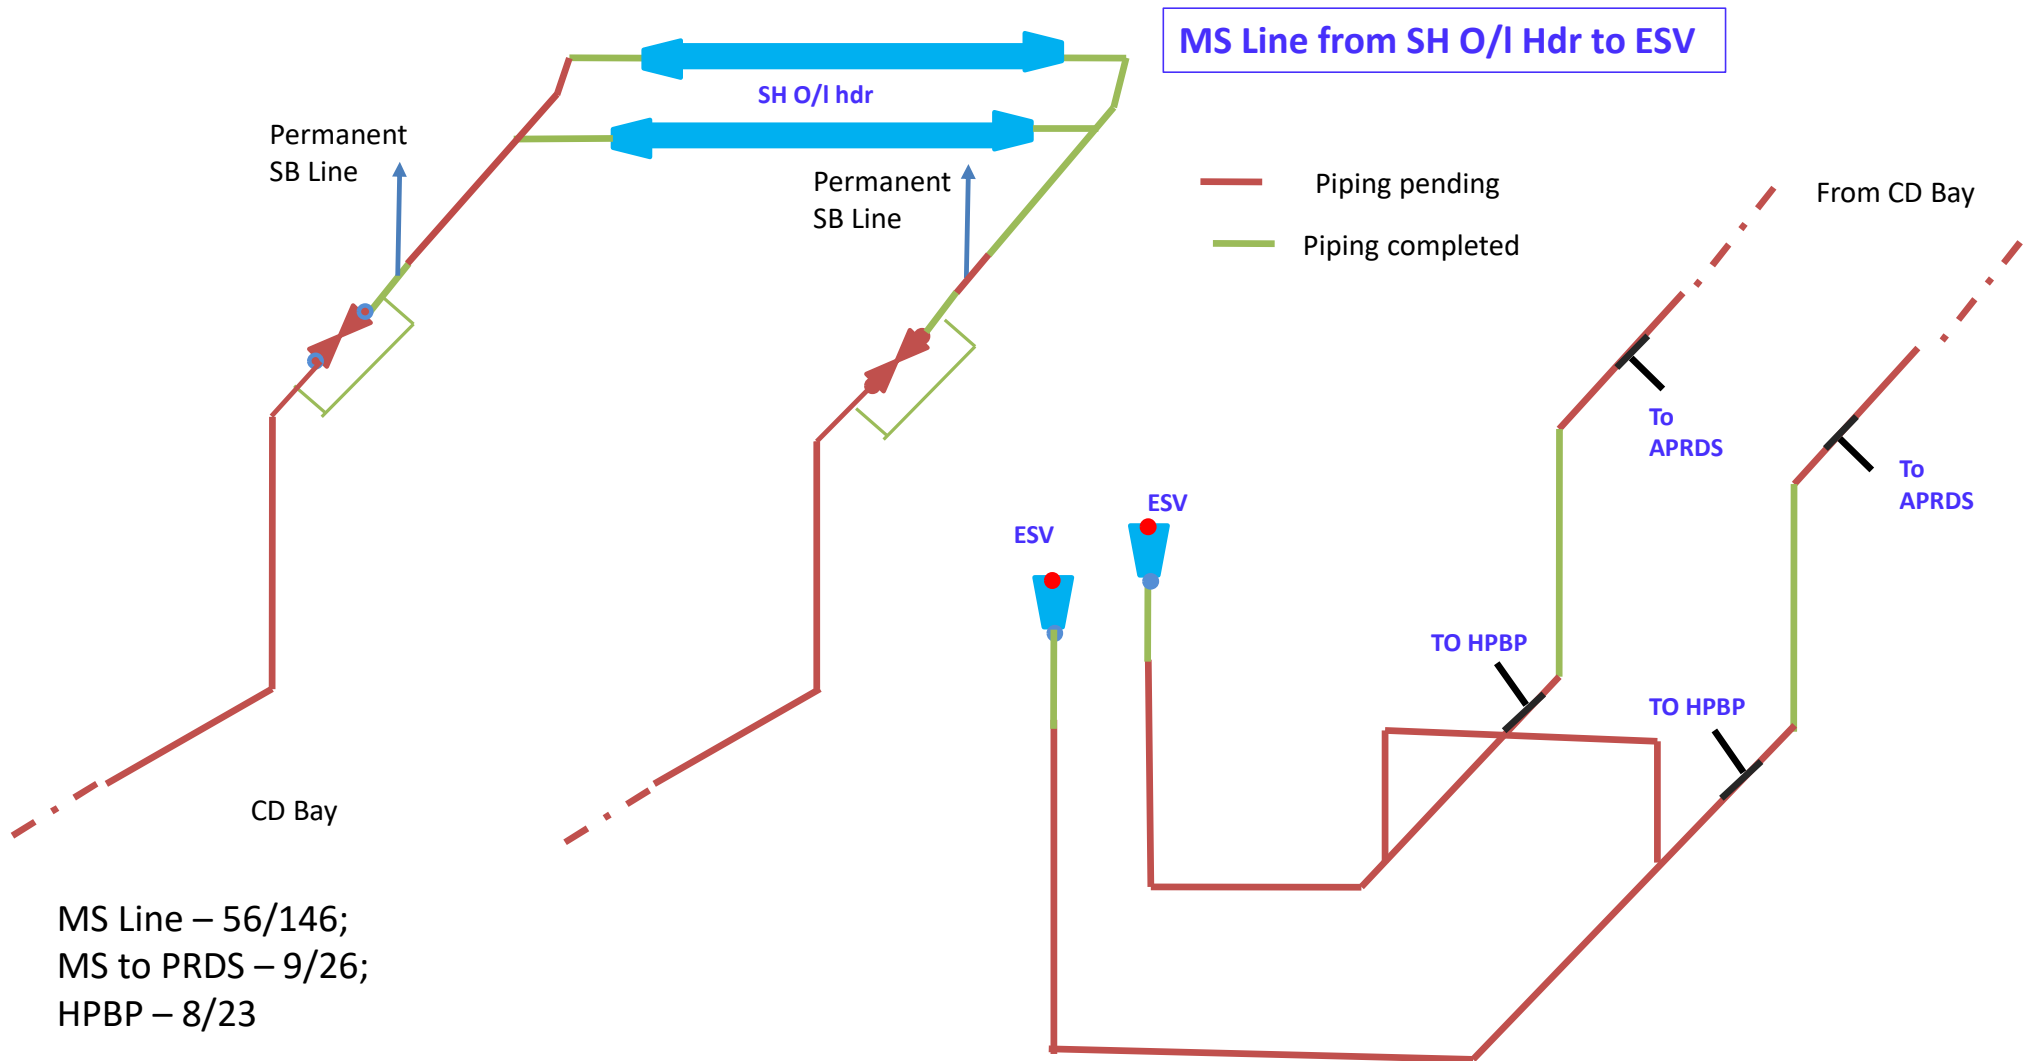

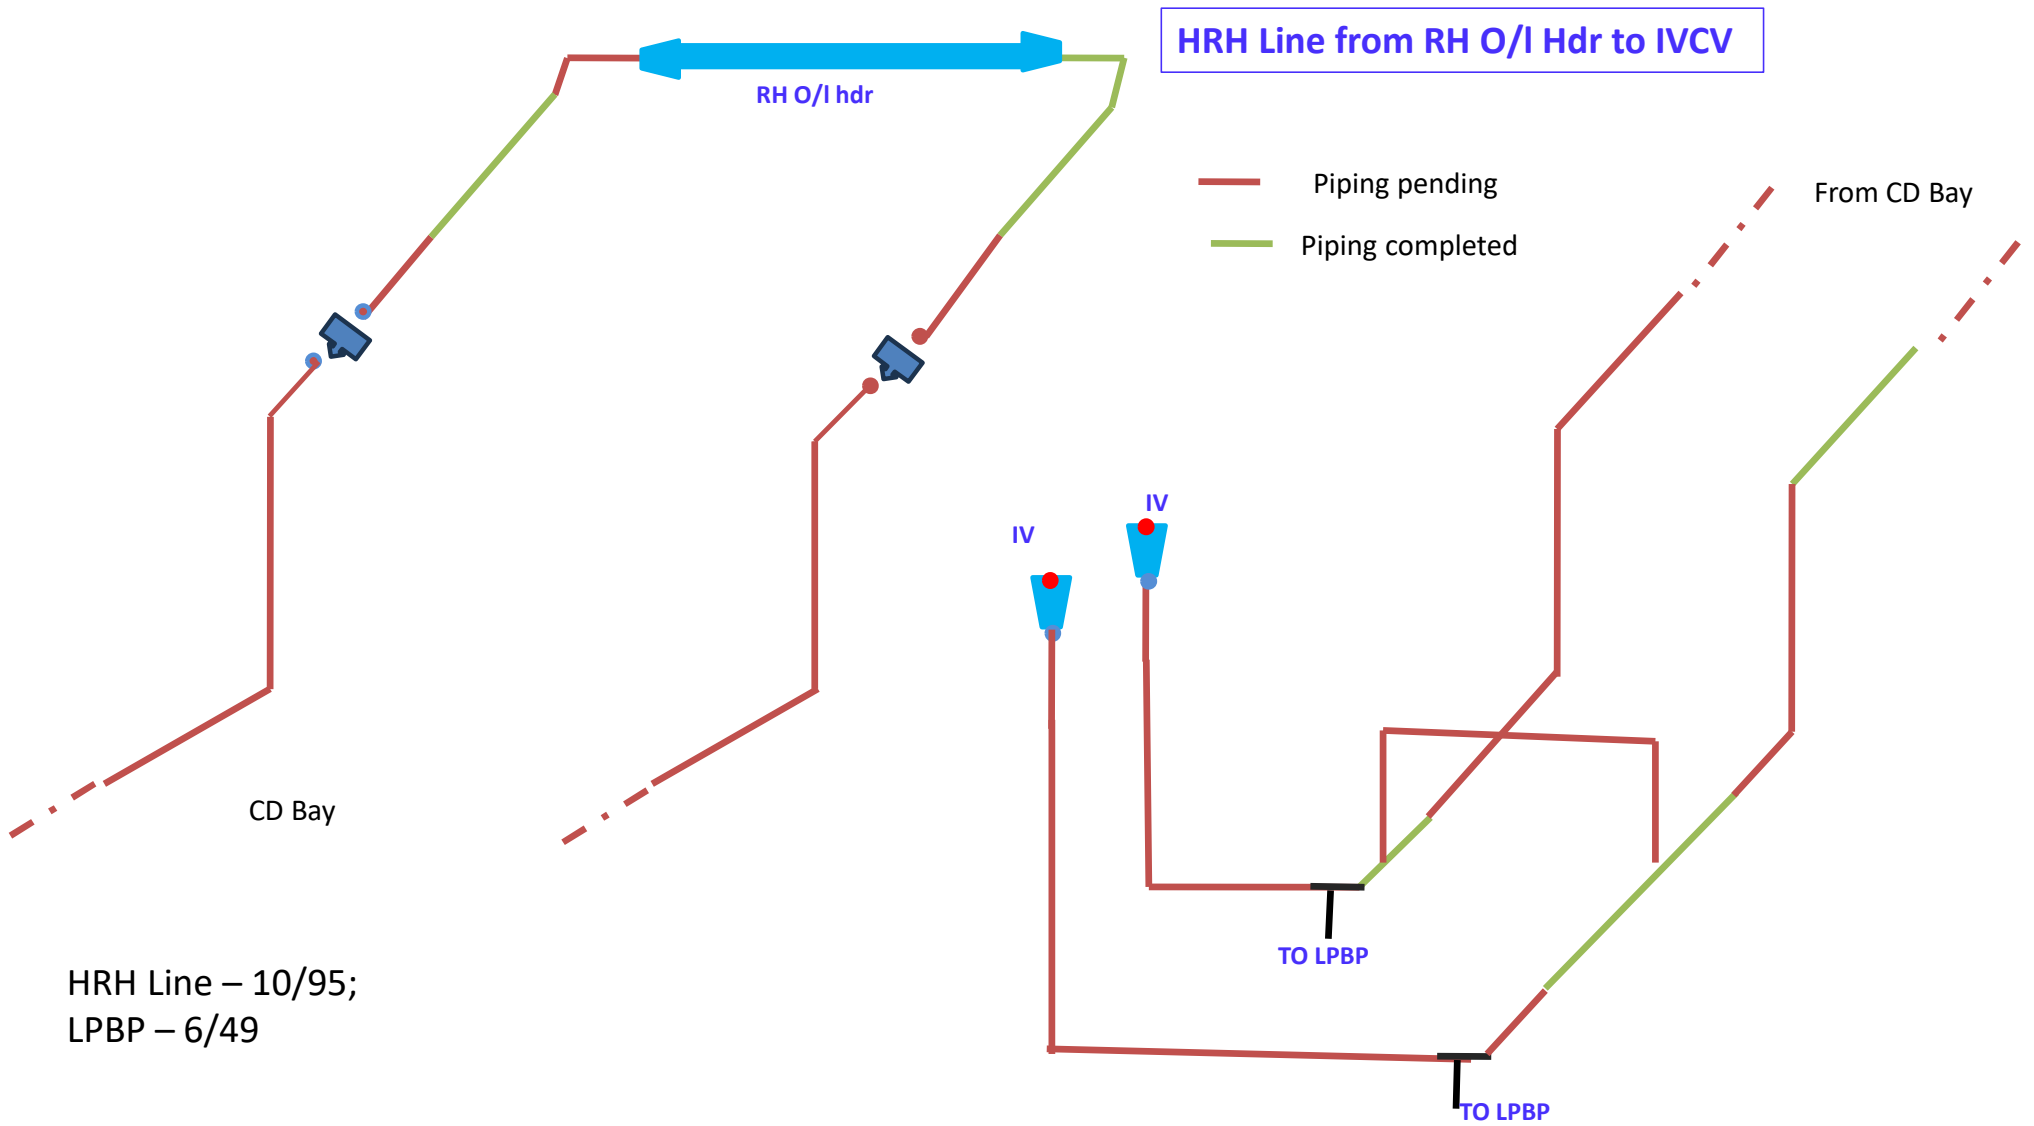

Unit 3 Milestones



Milestone	Target Dates	BHEL Commitments	Issues/Remarks
Boiler DHT	17.08.26	Completed	Completed
Boiler NDHT	25.09.26/ 15.10.26/ 18.11.26	18.11.26	Balance joints - 11628; Present progress rate 85 joints/day. Required – 200 joints/day. Balance SH – 6659; RH – 4969 joints
Boiler Light up	25.10.26/ 05.12.26	05.01.27	Boiler ducting works – Eco to ESP E and F pass, Boiler roof enclosure works; ST 2 charging – 30.08.26/15.09.26/25.09.26
Steam Blowing Completion	30.11.26/ 31.12.26	15.02.27	P91/92; Balance – 250 joints; July - 28 joints. Aug-26 joints. Required rate - 80/month MS incl PRDS – 65/172; HRH – 10/95; CRH – 14/87; LPBP – 6/49; HPBP – 8/23; BFD – 158/661 Hydro test of MS/CRH/HRH – 30.09.26/31.10.26; MDBP Trial – 20.10.26; TG Barring – 30.10.26/25.11.26
Sync	25.01.27/ 07.02.27	28.03.27	ACC Common duct ATT – 26.12.26; Flue can and duct completion – 25.12.25; TDBP 1B Trial – 15.01.27; ACC steam cleaning – 20.01.27; AHP readiness – 25.01.27
Full Load	20.02.27/ 25.02.27/ 10.03.27	25.05.27	Boiler ducting completion, ACC all 8 streets readiness – 15.02.27; Milling system and conveyor readiness – 15.02.27; 2 nd TDBP – 30.01.27; HPH readiness – 30.01.27
Trial Operation Completion	25.02.27/ 15.03.27	31.05.27	Ash Handling system stabilisation – 20.02.27



Unit 3 ESP – Present manpower deployed 47 nos



	Pass A	Pass B	Pass C	Pass D	Pass E	Pass F
Internals completion	Pending	Pending	Pending	Pending	In progress	In progress
Funnels completion	Pending for GD screen. Inlet -1 /2	Completed	Completed	Completed	Completed	Completed
Hoppers completion	14/20	0/20	0/20	18/20	Completed	Completed
ATT	Pending	Pending	Pending	Pending	Completed	Completed
Roof completion	Pending	Pending	Pending	Completed	Completed	Completed
Insulation	Not started	Not started	Not started	Not started	Not started	Can be started. Manpower constraints

Duct Structure and Duct - Total Ducting for BLU (RHS Path) – 430/552 modules still pending for erection.
 - Alignment and welding of hot sec air duct to windbox pending and erection of SOFA/OFA duct yet to be started

Manpower augmentation required

ESP – Available-50. Required -150 nos. Deficit – 100

Ducting – Available-100. Required -160 nos. Deficit – 60 (considering present material constraints)



ESP Roof status as on 14-09-26



Manpower Status - Unit 3




Agency	Required	Available on 09-07-26	Available on 21-07-26	Available on 08-08-26	Available on 23-09-26	Shortfall	Major Works Affected
Texcel- Boiler	1250	800	850	850	800	450	Non-drainable joints, Ducting, Roof enclosure, Platform works, Intermediate str
Texcel- Piping	400	120	200	200	250	150	MS/CRH/HRH joints. June:9 joints.July-28 Balance ~320 critical joints
A K Singhania	350	270	240	240	320	30	MPH RCC Columns, SG/MPH area paving
ElectroMech	150	130	100	0 60 (Rudra)	30 60 (Rudra)	60	ESP-CR, Drains and Paving works, BA Int silo, ISH, AHP MCC 3
Navnirman	400	320	320	240	280	120	ACC Night works yet to start
Sriram	300	40	75	80 (Elec) 30 (C&I)	130 (Elec) 70 (C&I)	100	*Electrical Labor license – 200 manpower *C&I Labor license – 70
Alpha	150	50	50	60	70	80	*2 shift working in TG TG Piping works to be started
Total	3000	1730	1835	1760	2010	990	



Boiler NDHT Progress



MONTH	Jan-26	Feb-26	Mar-26	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26
Plan (Joints)	428	1382	2240	3854	1748	2225	3930	6000	4590
Achieved	360	871	754	39	0	1005	737	713	1334
Backlog	68	511	1486	3815	1748	1220	3193	5287	3256
% Achieved	84%	63%	34%	1%	0%	45%	19%	12%	29%

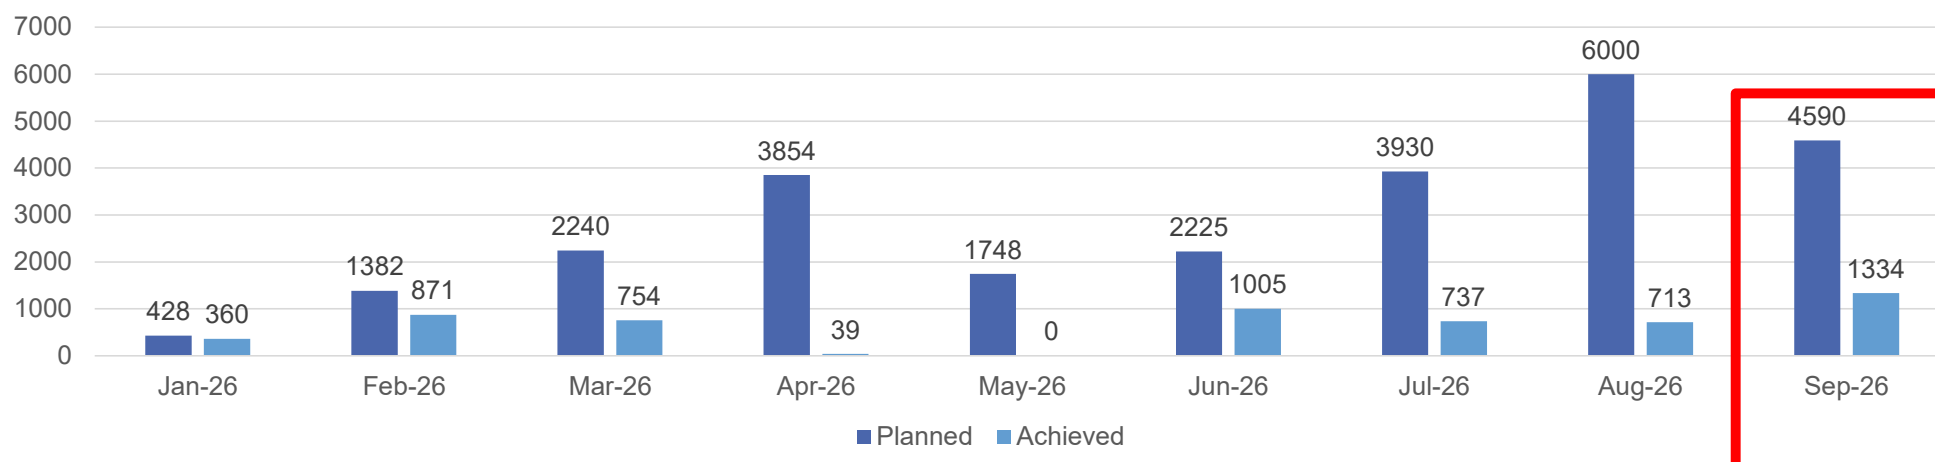

Support required – Manpower augmentation and heating agency technicians

